
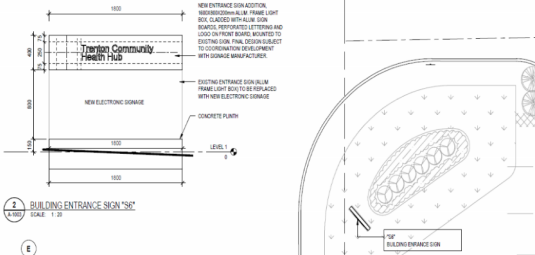




Q & A Log

250108 - BQWCHC-Trenton Community Health Hub

No	Date	Question	Response	Date Responded	Addendum Ref	Addendum Issue Date
1	10-Apr-26	1.Cash Allowances – In Section 01 21 00, 1.1.3, cash allowances are noted to cover door hardware and barrier-free door operators. Section 1.1.2.2 indicates that the cash allowances do not include installation costs. Since barrier-free door operators are typically supplied and installed by the same contractor, please clarify if the intention is to have separate suppliers for supply and installation, as this would be unusual.		10-Apr-26	AD-01	28-Apr-26
2	10-Apr-26	Structured Cabling System – Is PANDUIT an acceptable manufacturer for the structured cabling system?		10-Apr-26	AD-02	6-May-26
3	13-Apr-26	Could the timeline set out at GC 6.6.1 of the SGCs be amended from five (5) business days to ten (10) business days, such that the Contractor can ascertain whether such notice is truly necessary?		14-Apr-26	AD-01	28-Apr-26
4	15-Apr-26	The demolition plan legend on drawing A-101 denoted the existing slab to be prepared for a new floor finish. As per our site visit, this is a brand new slab. Please clarify whether minor floor patching for the new flooring is required, or if full floor levelling across the entire floor is anticipated. If full floor levelling is required, please advise the thickness to be included.	No new full floor levelling is required - patch and repair only	8-May-26		
5	15-Apr-26	<p>The wall at the door to Stair # 2 does not appear to receive any finishes as per drawing A-112. Please confirm this is correct. If this wall receives a drywall finish, please confirm electrical equipment will be removed and reinstalled as per electrical.</p> 			AD-01	28-Apr-26
6	15-Apr-26	<p>3.For the building entrance signage 2/A-1003,</p> <ul style="list-style-type: none"> •Can we get a shop drawing or further details of the existing sign? •For the addition on top, are we to price this based on the information provided, or is it carried in an allowance, as it says "final design to be developed with signage manufacturer. If pricing now, we will need to confirm what we are attaching to. •Are we to include the digital screen (s)? Is it single-sided or double-sided? Again, I will need to confirm the existing sign details so we can confirm the attachment. <p>ols there a spec of screen? i.e. dimension, pixel pitch, etc.? Is it the full 1800mm Wide x 800mm High?</p> <p>ols there a Cat 5/6 out to the sign for uploading content, or would it need to have line-of-sight Wi-Fi?</p> 			AD-01	28-Apr-26


Q & A Log

250108 - BQWCHC-Trenton Community Health Hub

No	Date	Question	Response	Date Responded	Addendum Ref	Addendum Issue Date
7	15-Apr-26	The scope of washroom accessories is not clear. Some are noted on drawing A-130. However, some accessories, such as grab bars, shower benches, Shower Curtains and hand dryers, are not clearly marked on drawings. Are these done by others? Most accessories are greyed out on elevations.			AD-01	28-Apr-26
8	16-Apr-26	Please confirm there are only two HSS support members to install at the two vestibule corners. Does detail 7/A-500 apply to the north vestibule? This detail calls the vestibule "Circulation 02". 			AD-01	28-Apr-26
9	16-Apr-26	Please confirm there are only two HSS support members to install at the two vestibule corners. Does detail 7/A-500 apply to the north vestibule? This detail calls the vestibule "Circulation 02".			AD-01	28-Apr-26
10	16-Apr-26	On drawing A-603, elevation 5, please confirm that the custom-printed film with branding and logos will be done by the owner. Or, is this the same as the glazing logo sign S9&S10 in detail 3&4/A-1003?			AD-01	28-Apr-26
11	16-Apr-26	On drawing A-801, under the owner-supplied/installed FFE schedule. Please confirm where it says owner supplied, vendor, installed, the owner will pay for the installation of their vendor.			AD-01	28-Apr-26
12	16-Apr-26	Please confirm that the work can be done during regular working hours for this project.			AD-01	28-Apr-26
13	16-Apr-26	Please advise who the base building contractors are. Is GC required to use the base building contractors?			AD-01	28-Apr-26
14	16-Apr-26	Is the ground finish at the location of the proposed generator interlock? (for cut and patch).	Yes - cut and provide new concrete slab sized per generator		AD-01 AD-02	2026-04-28 2026-05-06
15	16-Apr-26	Please confirm that the gas line for the proposed generator exists on site and can be utilized, as noted in Note #1 on drawing M03.	Existing gas line noted on M03 exists (photo below). Contractor to refer to sheet M05 for generator natural gas scope.	8-May-26		
						
16	16-Apr-26	Washroom Accessories: missing items on the schedule, who is supplying? L-bar, straight bars, Bradley shower seat and tilt mirrors. Is there a shower rod, are the garbage cans recessed or just in the room.			AD-01	28-Apr-26
17	17-Apr-26	In Section 23 07 13 (Mechanical Insulation) under 3.2.2.1 white aluminum jacketing is specified to be applied to exposed thermally insulated piping that is below 3m. Aluminum jacketing is not available in any colour other than natural aluminum. As an alternative, would you accept white PVC to be applied to all thermally insulated exposed piping?		21-Apr-26	AD-02	6-May-26
18	17-Apr-26	In Section 23 07 13 (Mechanical Insulation) under 3.2.3.5 white aluminum jacketing is specified to be applied to exposed thermally insulated ducts that are below 3m. Aluminum jacketing is not available in any colour other than natural aluminum. As an alternative, would you accept a smooth white five ply laminate, high performance cladding system with acrylic pressure sensitive self-adhesive (Ventureclad 1577CW-WM)?		21-Apr-26	AD-02	6-May-26

Q & A Log

250108 - BQWCHC-Trenton Community Health Hub

No	Date	Question	Response	Date Responded	Addendum Ref	Addendum Issue Date
19	17-Apr-26	Do acoustically lined ducts require thermal insulation? Typically, acoustically lined ducts are not thermally insulated. Please confirm if this is required.		21-Apr-26	AD-02	6-May-26
20	17-Apr-26	Can you please confirm who the BAS controls contractor is?		21-Apr-26	AD-02	6-May-26
21	17-Apr-26	Can you please confirm the hours of work are all afterhours except mechanical room work as per section 23 05 00.			AD-02	6-May-26
22	17-Apr-26	As per section 23 31 00, existing duct systems, who is responsible for installing duct sanitizing ports? Would this be under a duct cleaner scope?		21-Apr-26	AD-02	6-May-26
23	20-Apr-26	In the ADA Washrooms, are there Shelves, a fold-down grab bar beside the toilet, a Man Table, and Coat Hooks? In the Tub Room, are there shower shelves and Towel bars?			AD-01	28-Apr-26
24	21-Apr-26	<p>Could you please confirm which wall assemblies correspond to those highlighted in red on the drawings? Your clarification will assist us in ensuring accurate interpretation and pricing.</p> 			AD-01	28-Apr-26
25	22-Apr-26	<p>There is Resinous Flooring section in the spec, but looking at the floor finishing plan I can't seem to find the area.</p> <p>The finish schedule says EP is Sika but once again I can't seem to find where its to be applied.</p>			AD-01	28-Apr-26
26	22-Apr-26	<p>It appears that they will be adding onto some of their existing security systems at this site, according to the spec. Unfortunately they don't mention the make / model of cameras desired, or what their existing head-end VMS is, so it will be hard to know what cameras are compatible and what camera licensing they require.</p> <p>For the alarm system (EPPS), they mention a DSC Maxsys 4020 panel and an LED annunciator panel. Please note that the DSC Maxsys is considered end-of-life and should be replaced with the DSC Neo product line. They also no longer make an LED annunciator panel for the old Maxsys or the new Neo product, so that will have to be excluded. I don't see any keypad locations on the drawings, so perhaps they are existing ?</p> <p>Are you able to find out more information on this one ?</p> <p>Do they have an existing EPPS system on-site ? If so, what is it.</p> <p>Do they need remote monitoring of the EPPS alarm system ?</p>			AD-02	6-May-26
27	24-Apr-26	<p>1. Section 09.21.16. 2.2.25 gypsum board trims - can you please confirm is the bullnose corners are required. If so, can you please confirm which locations they are required?</p> <p>2. Section 09.21.16. 2.2.37 - can you please confirm if these reveal trims are required. If so, can you please confirm which locations they are required?</p>	<p>1. Bullnose corners are not required</p> <p>2. Reveal trims not required.</p>	8-May-26	AD-03	
28	27-Apr-26	<p>1.Re: Door Schedule Door D1.005 references the frame to be HM but the finish (WV) and similar rooms reference WD frames, please advise if to be HM or WD.</p> <p>2.Re: Interior Screens Screens SCR-004 and SCR-003 are shown on screen schedule to be HM but the details for the screen show ALUM, please confirm material.</p>	<p>1. Frame should be WD to match other similar frames.</p> <p>2. The interior screen and details to match material on screen schedule</p>		AD-02	6-May-26
29	27-Apr-26	<p>Would it be possible to provide the make and model of the existing NVR system and cameras?</p> <p>The bid form PDF appears to be secured. Could you please provide the password or an unlocked version for completion</p>	<p>1. This information will be available to the selected bidder.</p> <p>2. The PDF of the bid form should not be locked. You should be able to print it and fill it in.</p>	29-Apr-26		


Q & A Log

250108 - BQWCHC-Trenton Community Health Hub

No	Date	Question	Response	Date Responded	Addendum Ref	Addendum Issue Date
30	27-Apr-26	<p>Sign type S6</p> <ul style="list-style-type: none"> - Are there drawings of the existing d/s pylon sign that we are meant to be modifying? - Are there drawings for the new additions to the pylon? - Is the digital display also done by the signage vendor? If so, would you be able to provide specifications? <p>Sign types S9 & S10</p> <ul style="list-style-type: none"> - Could you please clarify what is meant by "extent on vinyl signage"? <p>Sign type IN</p> <ul style="list-style-type: none"> - Appears on interior signage schedule but does not have its own drawing. Would it be possible to provide a design or additional details? <p>Sign type ES</p> <ul style="list-style-type: none"> - Appears twice on interior signage schedule (meeting room signage, once as medium, another as large). Can you confirm if both are to follow the sizing/construction on drawing? 	<p>Sign S6 - shop drawing provided in AD-01 for existing signage</p> <p>Sign S9 , S10 - should read 'EXTENT OF...'</p> <p>Sign IN - drawing provided in AD-01</p> <p>Sign ES - rooms say either 'Large' or 'Medium' on room tag</p>		AD-01	28-Apr-26
31	27-Apr-26	<p>- "In Section 23 07 13 (Mechanical Insulation) under 3.2.2.1 white aluminum jacketing is specified to be applied to exposed thermally insulated piping that is below 3m. Aluminum jacketing is not available in any colour other than natural aluminum. As an alternative, would you accept white PVC to be applied to all thermally insulated exposed piping?"</p> <p>•"In Section 23 07 13 (Mechanical Insulation) under 3.2.3.5 white aluminum jacketing is specified to be applied to exposed thermally insulated ducts that are below 3m. Aluminum jacketing is not available in any colour other than natural aluminum. As an alternative, would you accept a smooth white five ply laminate, high performance cladding system with acrylic pressure sensitive self-adhesive (Ventureclad 1577CW-WM)?"</p> <p>•"Do acoustically lined ducts require thermal insulation? Typically, acoustically lined ducts are not thermally insulated . Please confirm if this is required."</p> <p>•"Can you please confirm who the BAS controls contractor is?"</p> <p>•"Can you please confirm the hours of work are all afterhours except mechanical room work as per section 23 05 00."</p> <p>•"As per section 23 31 00, existing duct systems, who is responsible for installing duct sanitizing ports? Would this be under a duct cleaner scope?"</p> <p>•"Can we get a shop drawing or further details of the existing sign?"</p> <p>•"For the addition on top, are we to price this based on the information provided or is it carried in an allowance as it says 'final design to be developed with signage manufacturer. If pricing now we will need to confirm what we are attaching to."</p> <p>•"Are we to include the digital screen (s)? Is it single sided or double? Again, I will need to confirm the existing sign details so we can confirm attachment."</p> <p>•"Is there a spec of screen? i.e. dimension, pixel pitch etc? is it the full 1800mm Wide x 800mm High?"</p> <p>•"Is there a cat 5/6 out to the sign for uploading content or would it need to have line of sight wifi?"</p> <p>•"On the exterior pylon is it currently 1800 by 800 and we're adding an additional 400mm in height?"</p> <p>•"By Perforated lettering are we speaking to day/night lit letters?"</p> <p>•"By Electronic sign do they want to display pictures and text messages here that are changed remotely?"</p> <p>•Section 09.21.16.2.2.25 gypsum board trims - can you please confirm is the bullnose corners are required. If so, can you please confirm which locations they are required?</p> <p>•Section 09.21.16.2.2.37 - can you please confirm if these reveal trims are required. If so, can you please confirm which locations they are required?</p>			AD-01 AD-02	2026-04-28 2026-05-06
32	27-Apr-26	<p>•Could you please confirm which type of cove base we should consider for this project: a site-fabricated integral cove base or a prefabricated one?</p> <p>•The specification of sheet flooring has listed bot.</p> <p>•Please note that prefabricated wall base is no longer available in Canada, so it will be an expensive option as it will require two-way shipping, customs duty charges and additional time for wall base production.</p>			AD-02	6-May-26
33	27-Apr-26	I am writing to resubmit, in the proper format, our request for approval of an alternate manufacturer for the aluminum windows and doors.	Use what is specified.	28-Apr-26		

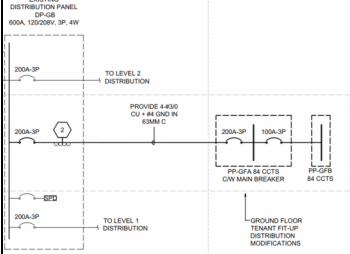
Q & A Log

250108 - BQWCHC-Trenton Community Health Hub

No	Date	Question	Response	Date Responded	Addendum Ref	Addendum Issue Date																																																																																										
34	28-Apr-26	<p>• We noted that the specification for sign type “IN” is missing. Could you please issue an RFI to obtain this information?</p> <table><tr><td>IN</td><td>021</td><td>MEETING ROOM - LARGE</td><td>1.021</td><td>1</td><td>Maximum 59 people</td></tr><tr><td>ES</td><td>021</td><td>MEETING ROOM - LARGE</td><td>1.021</td><td>1</td><td>"Hastings Room"</td></tr><tr><td>RS</td><td>022</td><td>STORAGE</td><td>1.022</td><td>1</td><td>"Storage Room"</td></tr><tr><td>RS</td><td>023</td><td>STAFF LOUNGE</td><td>1.023</td><td>1</td><td>"Coffee Bar"</td></tr><tr><td>VA</td><td>024</td><td>CIRCULATION</td><td>42</td><td>1</td><td>"STAFF ONLY"</td></tr><tr><td>RS</td><td>026</td><td>COUNSELLING ROOM</td><td>1.026</td><td>1</td><td>"Counseling Room 6"</td></tr><tr><td>RS</td><td>027</td><td>COUNSELLING ROOM</td><td>1.027</td><td>1</td><td>"Counseling Room 7"</td></tr><tr><td>RS</td><td>028</td><td>SHARED OFFICE</td><td>1.028</td><td>1</td><td>"Southeast Public Health Office"</td></tr><tr><td>RS</td><td>029</td><td>COUNSELLING ROOM</td><td>1.029</td><td>1</td><td>"Counseling Room 4"</td></tr><tr><td>NP</td><td>030</td><td>MANAGER OFFICE</td><td>1.030</td><td>1</td><td>CMHA Manager Office</td></tr><tr><td>RS</td><td>031</td><td>COUNSELLING ROOM</td><td>1.031</td><td>1</td><td>"Counseling Room 3"</td></tr><tr><td>RS</td><td>032</td><td>COUNSELLING ROOM</td><td>1.032</td><td>1</td><td>"Counseling Room 2"</td></tr><tr><td>RS</td><td>033</td><td>PHONE ROOM</td><td>1.033</td><td>1</td><td>"Phone Room"</td></tr><tr><td>BF</td><td>034</td><td>BF W.C.</td><td>1.034</td><td>1</td><td></td></tr><tr><td>RS</td><td>035</td><td>JANITOR</td><td>1.035</td><td>1</td><td>"Janitor"</td></tr></table> 	IN	021	MEETING ROOM - LARGE	1.021	1	Maximum 59 people	ES	021	MEETING ROOM - LARGE	1.021	1	"Hastings Room"	RS	022	STORAGE	1.022	1	"Storage Room"	RS	023	STAFF LOUNGE	1.023	1	"Coffee Bar"	VA	024	CIRCULATION	42	1	"STAFF ONLY"	RS	026	COUNSELLING ROOM	1.026	1	"Counseling Room 6"	RS	027	COUNSELLING ROOM	1.027	1	"Counseling Room 7"	RS	028	SHARED OFFICE	1.028	1	"Southeast Public Health Office"	RS	029	COUNSELLING ROOM	1.029	1	"Counseling Room 4"	NP	030	MANAGER OFFICE	1.030	1	CMHA Manager Office	RS	031	COUNSELLING ROOM	1.031	1	"Counseling Room 3"	RS	032	COUNSELLING ROOM	1.032	1	"Counseling Room 2"	RS	033	PHONE ROOM	1.033	1	"Phone Room"	BF	034	BF W.C.	1.034	1		RS	035	JANITOR	1.035	1	"Janitor"			AD-01	28-Apr-26
IN	021	MEETING ROOM - LARGE	1.021	1	Maximum 59 people																																																																																											
ES	021	MEETING ROOM - LARGE	1.021	1	"Hastings Room"																																																																																											
RS	022	STORAGE	1.022	1	"Storage Room"																																																																																											
RS	023	STAFF LOUNGE	1.023	1	"Coffee Bar"																																																																																											
VA	024	CIRCULATION	42	1	"STAFF ONLY"																																																																																											
RS	026	COUNSELLING ROOM	1.026	1	"Counseling Room 6"																																																																																											
RS	027	COUNSELLING ROOM	1.027	1	"Counseling Room 7"																																																																																											
RS	028	SHARED OFFICE	1.028	1	"Southeast Public Health Office"																																																																																											
RS	029	COUNSELLING ROOM	1.029	1	"Counseling Room 4"																																																																																											
NP	030	MANAGER OFFICE	1.030	1	CMHA Manager Office																																																																																											
RS	031	COUNSELLING ROOM	1.031	1	"Counseling Room 3"																																																																																											
RS	032	COUNSELLING ROOM	1.032	1	"Counseling Room 2"																																																																																											
RS	033	PHONE ROOM	1.033	1	"Phone Room"																																																																																											
BF	034	BF W.C.	1.034	1																																																																																												
RS	035	JANITOR	1.035	1	"Janitor"																																																																																											
35	28-Apr-26	<p>Please remove requirements for specified signage manufacturers from the scope since they are from BC and Georgia. Quality requirements specified should be sufficient.</p> <p>Meeting room interior signage- Type IN " Max.59 people". Can you please provide the specifications and drawing for this sign. We were not able to find it in the current signage schedule.</p> <p>Please provide a one week extension to the closing date.</p>			AD-01	28-Apr-26																																																																																										
36	28-Apr-26	<p>As per mechanical specification any work outside the mechanical rooms need to be completed afterhours. Please confirm this requirement.</p>			AD-02	6-May-26																																																																																										
37	29-Apr-26	<p>1. Can you please provide structural drawings, this is required to see where beams with sprayed fireproofing are located for new drywall installations.</p> <p>2. Can you please confirm the manufacturer and product required for the mullion extenders?</p> <p>3. We contacted Trinity fire and security as addendum # 1 named them as base building contractor. They informed us that they cannot work in this building because of the type of panels on site. They said they do not have rights to work on those panels. Please revisit this requirement and advise who the base building contractor is or who we should contact.</p> <p>4. Addendum # 1 shows Trinity Fire and Security for Sprinkler / Fire Suppression System. We contacted them and they informed us that they only complete fire alarm system in buildings that they can work on (not this building) and they sub out the sprinkler work to others. Please separate these for whoever else you introduce for base building contractors.</p> <p>5. Addendum # 1 named Siemens for HVAC/BAS does this mean the BAS is to be done by Siemens? Or HVAC and BAS both should be done by Siemens?</p>	<p>1. Structural drawings for reference included in AD-03</p> <p>2. Mullion extenders sufficiently detailed in drawing.</p> <p>3. There is no requirement for special sprinkler company to work on the sprinklers in this building. New HVAC work can be executed by contractor of choice.</p> <p>4. Anyone can work on the fire alarm in this building - no requirement. The existing system is an EDWARDS systems. Installers must be certified to work on and provide Edwards Fire alarm systems.</p> <p>5. Siemens is the current vendor of the BAS systems.</p>		AD-02 AD-03	5 May 2026 8 May 2026																																																																																										
38	29-Apr-26	<p>Secondly, we would like to inquire whether the deadline for Questions and Clarifications will also be extended in light of the revised closing date.</p>	<p>Yes the period of questions will also be extended. We will clarify.</p>	29-Apr-26																																																																																												
39	30-Apr-26	<p>•Due to the commitment to previous bids, can you please kindly move the tender closing to May 14 (on Thursday)? We have tenders due on May 12 and May 13 at the same time (by 2PM). If the extension can not be granted, we may not be able to submit the bid.</p> <p>•Addendum 01 clarified that the Cash Allowance for Door Hardware (including barrier-free door operators) is to supply only. For the automatic door operators, the specialized contractor (not the door & hardware contractors) will supply and install for the scope during construction. Can you please include the installation cost of the door operators in the Cash Allowance?</p>	<p>will be extended until May 14th</p>		AD-02	5-May-26																																																																																										

Q & A Log

250108 - BQWCHC-Trenton Community Health Hub

No	Date	Question	Response	Date Responded	Addendum Ref	Addendum Issue Date
40	30-Apr-26	<p>I am writing to formally request an amendment to the closing date and the RFI deadline on the Merx platform. Although the revised closing date has been communicated through an addendum, we note that the platform has not yet been updated accordingly. This discrepancy raises concerns regarding our ability to submit the proposal by May 12. We kindly request that the Merx posting be updated to reflect the revised timelines.</p> <p>Additionally, we would appreciate clarification on the following items:</p> <p>1. Within the Contractor Installed Fee Schedule, items E10, E25 (refrigerator), E41, E42, E44, E46, and E47 (as referenced on drawing A-130) are listed; however, these items could not be located on the drawings. Please confirm whether these items are to be included in the scope and provide the corresponding quantities for each.</p> <p>2. EP-1 (Epoxi flooring) is indicated on the Finish Schedule but is not shown or tagged on the drawings. Kindly clarify its intended location and application.</p>	<p>Merx posted was updated</p> <p>1. E10 is shown on drawing 4/A-401. E25 is located in room 1.023. E41 is located in rooms 1.008, 1.009, 1.013, 1.021. E42 is located in room 1.021. Refer to addendum 3 for E44, E46, E47</p> <p>2. There is no epoxy flooring in this project</p>		AD-01 AD-02 AD-03	28-Apr-26
41	1-May-26	<p>1. The vinyl flooring products on the spec sheet being discontinued. All four options are showing as dropped products (VF1, VF2, VF3 & VF4).</p>			AD-03	8-May-26
42	4-May-26	<ul style="list-style-type: none"> • Chemical treatment for piping: Section 23 25 00 missing on the spec provided. • Bulkheads: missing height. Assuming 1.25m high. Please confirm. • HSS Support: addendum #1 clarified the HSS Support on Vestibule and Activity room, however we are still missing the specs for the HSS Support on the remaining rooms. • Please advise the expected completion date for this project 	<p>1. Addressed in AD-02</p> <p>2. All ceiling and bulkhead heights are noted on drawings.</p> <p>3. HSS is only required where noted on the drawings</p> <p>4. GC to provide expected completion date based on construction.</p>		AD-02	6-May-26
43	4-May-26	<p>please advise the manufacturer of the existing submetering system as per note 2 on the SLD:</p> <p>2. PROVIDE NEW 200A 3P HFD SERIES BREAKER IN DP-GB FOR NEW TENANT PANELS. PROVIDE NEW SUBMETERING TO MATCH EXISTING METERS FOR EXISTING FLOOR TENANTS. COORDINATE WITH EXISTING THIRD PARTY METERING VENDOR AND PROVIDE AS REQUIRED.</p>				
44			Existing looks to be a Carma Metering System			

Q & A Log

250108 - BQWCHC-Trenton Community Health Hub

No	Date	Question	Response	Date Responded	Addendum Ref	Addendum Issue Date
45	5-May-26	<p>The notes indicate to reuse existing mains and branch piping where possible and to modify as required for the new layout. However, we're not seeing any existing piping shown on the plan—only three heads in the mechanical room, which we're assuming are existing as they're the only ones indicated.</p> <p>There's a note to remove all existing sprinkler heads within the area of work, but the plan doesn't appear to show any beyond those noted. Please provide existing sprinkler piping layout.</p> <p>The scope indicates modifications and additions to an existing video management system; however, the specifications do not identify the current system's manufacturer or model.</p> <p>There is no mention of the required video storage retention period. With the increase from 4 to 7 cameras, additional storage capacity may be needed.</p> <p>The project notes 7 existing card reader doors and 15 new ones to be added. Are the existing doors connected to a Kantech system? If so, should we be expanding the existing system or providing a new Kantech license?</p> <p>Are we required to provide new servers or workstations for the access control system?</p> <p>Are we required to provide a network switch for the video management system or will it be provided by the client?</p> <p>Will the system require remote offsite access for which we will need coordination with the IT department?</p>			AD-02	06 May 2026
46	5-May-26	Do you know what products the owner will be supplying in regard to the automatic operators and push/wave switches? The price would all really depend on that.	The owner is not supplying them. They will be provided from the cash Allowance. Refer to Section 08 71 00 clause 2.2.18 for the basis of design	8-May-26		
47	5-May-26	Please confirm wrap-up insurance is required for this project as noted in the specifications. This is a minimum of \$10K charge to carry in our price.	Refer to Section 01 73 00 Supplementary Conditions, GC 11.1 for the project insurance requirements.	8-May-26		
48	6-May-26	Can you please ask architect if there can be any substitute for photopolymer substrate for interior sign The reason is photopolymer is extremely expensive as there is a scarcity of suppliers and all in USD.	Substitute can be provided if proper submittals are submitted and it have the same performance specs as originally specified.	8-May-26		
49	6-May-26	<p>Could you please confirm the locations of the wall tile backsplashes (T3 & T4), as they do not appear on the drawings?</p> <p>Please clarify the floor level. All mechanical drawings are called basement drawings. The architectural drawings are all called ground floor. Please clarify if the drawings are all for the same floor</p>	<p>1. T3 & T4 are not used unless noted on drawings.</p> <p>2. This floor is technically the basement (below grade in some areas) There are two finished floors above. The drawings are all for the same level.</p>	8-May-26		
50	6-May-26	I've reached out to the supplier of the AU.DIGROOVE AG10-280 Flat cut walnut, Clear finish. They have declined to bid because the work is too small to quote. Please specify an alternate material for WD1.	Product needs to match so please go to a different supplier	8-May-26		
51	6-May-26	Could you please confirm the locations of the wall tile backsplashes (T3 & T4), as they do not appear on the drawings?	T3 & T4 are not used unless noted on drawings.	8-May-26		

Q & A Log

250108 - BQWCHC-Trenton Community Health Hub

No	Date	Question	Response	Date Responded	Addendum Ref	Addendum Issue Date
